RASTA
Center for Road Technology

Letter No: RAS/ Con/ 15-16/ 519

To,
The Commissioner,
Office of the Commissioner, BBMP Head Office,
N.R.Circle,
Bangalore.

Date: 16.06.15

Dear Sir,

Ref: Your letter No. A/PR/G667/15-16 dated 02-05-2015
Sub: Inspection of Completed works and Pending Bills

With reference to the above subject the Inspection of the following works of Ward no. 7, Kodigehalli Sub Division, Byatarayanapura has been completed and the Inspection Report is enclosed for your reference.

1. Improvement to Roads and drains from NH-7 to Jakkur Kaval Road in Ward No 7 Kodigehalli Sub Division (Sl. No. 1)
2. Improvement of Roads in Muneshwara swamy Temple roads and cross roads at Amruthahalli in ward No.7 Kodigehalli Sub Division(Sl. No.2)
3. Improvements of Roads, drains and culverts in main Roads and Cross roads in Hottappa Layout in ward No. 7, Kodigehalli sub division (Sl. No.6)
4. Improvements to Road drains and asphalting to roads in Vinayaka L/O 1st main, 2nd stage in Ward No:07 Byatarayanapura in Kodigehalli sub division (Sl. NO. 8)
5. Improvement to Road drains and Asphalting to roads in Vinayaka L/O 2nd cross, 1st stage in ward no:07, Byatarayanapura in kodigehalli sub division (Sl. NO.9)
6. Improvement to Road drains and Asphalting to roads in Vinayaka L/O 2nd main, 2nd stage in ward no:07, Byatarayanapura in kodigehalli sub division (Sl. No.10)

RASTA-Resource Centre for Asphalt and Soil Training Academy, VOLVO Construction Equipment Road Machinery Campus, # 7 & 8 ,Peenya Industrial Area, Bangalore – 560 058, India
Tel: 91-080-22192500, Fax: 91-080 - 28375483 / 28394651, e-mail: group.rasta@rastaindia.com

7. Improvement to Road drains and Asphalting to roads in Venkanagowda layout Kempapura 1st B Main in Ward No.07 (Sl. NO.12)
8. Improvements of Roads and construction of RCC drain in "A" Block Sahakarnagar in Ward No.07, Kodigehalli Sub division (Sl. NO. 13)
9. Improvement of Roads and drains in Vayunnadara layout and Nethajinagar in ward No.7 Kodigehalli Sub Division (Sl. NO. 14)
10. Construction of dry waste collection centre at Amruthanagara in Ward no:07 of Kodigehalli Sub division (Sl. NO. 17)
11. Construction of RCC drain at Maramma Temple main road in Amruthahalli in Ward No. 07 K.S.D (Sl. No. 18)
12. Providing and Fixing name boards in Vinayaka and Venkatagowda Layout in Ward No.07 Byatarayanapura, Kodigehalli sub division (Sl. NO. 19)
13. Improvements of Concrete roads and drains at Byatarayanapura in Ward No.07 of Kodigehalli sub division (Sl. NO. 28)
14. SC / ST Houses Bill (6 items)

Please do the needful.

Regards,

Dr. Krishnamurthy
Professor – PG studies & STA
RASTA

Copy to:

1. Executive Engineer, BBMP Yelahanka

Dr. Krishnamurthy
Professor - PG Studies
RASTA Centre for Road Techn
VOLVO Construction Equipme
Phase I, Peenya Industrial Ar
Bangalore - 560 058, India

RASTA
Center for Road Technology

BRUHAT BANGALORE MAHANAGARA PALIKE
INSPECTION REPORT

Sl No	Item	Description
1	Name of Work	Construction of RCC drain at Maramma Temple main road in Amruthahalli in Ward No. 07 K.S.D (Sl. No. 18)
2	Estimate Cost	19.50 lakhs
3	Administrative Approval No and Date	JC/YEL/AA/194/12-13 dated 14/5/12
4	Technical sanction No. and Date	EE/BTP/TS/89/12-13 dated 15/5/12
5	Job Code No. and P Code No.	007-12-000054 P.1771
6	Tender Direct Entrested to KRIDL	Data not available
7	If Tender, Tender Notification No. Date and Publication in daily news Paper	EE/BTP/BBMP/E-TND/02/12-13 dated 15/5/12 Vijaya Karnataka 27/5/12
8	Tender Approved Details	Data not available
9	Work Order No and Date	EE/BTP/BBMP/E-TND/187/12-13 dated 15/11/12
10	Stipulation time of Completion	60 days
11	Actual Date of Commencement	Data Not available
12	Actual Date of Completion	28/9/13
13	Delay if any	Data Not available
14	Reson for Delay	Data Not available
15	Payment made till date.	Data Not available
16	BR NO. and Date	236 dated 28/9/13
17	Status of Work	Completed

18	Photograph verfied	Yes
19	Date of Inspection	27.05.15
20	MB No. and Page No.	Data Not available
21	Test Result	--
22	Section officer	Basvaraju
23	Sub Division Officer	K P Neelakantaiah
24	Observation	Please Refer Anncxure -2
a	Work Quality	Satisfactory
b	Comments	The drains and culverts have been constucted according to specifications as mentioned in the estimate.The works stands completed as on date and is found satisfactory the Bill may be considered for clearance.

Executive Engineer
Byatarayanapura Div.
Yalahanka Zone, B.B.M.P.
Bangalore-560092

Dr. Krishnamurthy
Professor - PG Studies
RASTA Centre for Road Technology
VOLVO Construction Equipment Campus
Phase I, Peenya Industrial Area
Bangalore – 560 058, India

RASTA
Center for Road Technology

BRUHAT BANGALORE MAHANAGARA PALIKE

ANNEXURE 2- INSPECTION REPORT - OBSERVATIONS

Name of the Work: Construction of RCC drain at Maramma Temple main road in Amruthahalli in Ward No. 07 K.S.D (Sl. NO. 18)					
Sl No	Item	Measurements and Qty as per Claims (MB & Bills)	Measurements and Qty as per Actuals	Deviation	% Deviation
1	Length of drain	800m	800m	nil	nil
2	Depth of drains	600mm	600mm	nil	nil
3	No. of culverts (Deck Slab)	2	2	nil	nil

Dr. Krishnamurthy
Professor - PG Studies
RASTA Centre for Road Technology
VOLVO Construction Equipment Campus
Phase I, Peenya Industrial Area
Bangalore – 560 058, India

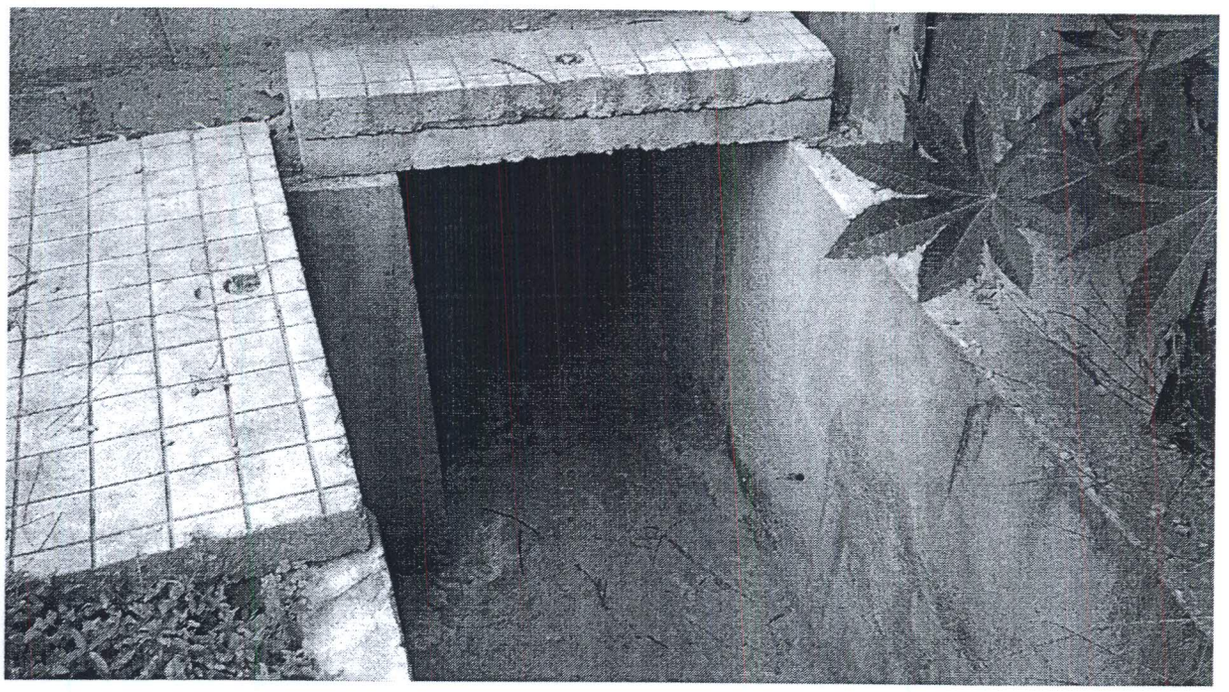

Construction of RCC drain at Maramma Temple main road in Amruthahalli in Ward No. 07 K.S.D (Sl. No. 18) - Satisfactory
